



**ST. JOSEPH'S A. MCKAY ELEMENTARY SCHOOL
PROJECT STATUS REPORT
August 2023**

New grades PP-6 replacement school project in north end Halifax
Modern, daylight filled learning environment, maximizing use of existing site Main floor area, accessible for after hours public use Large, central atrium, connecting all floors Integrated childcare centre Classroom areas w/ open, collaborative spaces


General Project Information		Contacts re: concerns or questions	
Project Sponsor Group	NS Dept. of Public Works NS Dept. of Education and Early Childhood Development Halifax Regional Centre for Education	Construction related	John Rhynold, Marco Site Superintendent, During regular business hours at 902-209-4399 or jrhynold@marcogroup.ca
Design Consulting	Stantec Architecture Ltd.	General Project	Ed Burley, DPW Project Manager During regular business hours at 902-483-6143 or ed.burley@novascotia.ca
General Contractor	Marco Group		

2023												2024								
2022-23 SCHOOL YEAR				SUMMER BREAK		2023-24 SCHOOL YEAR						SUMMER BREAK								
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep		
					CURRENT MONTH				CHRISTMAS										TARGET OCCUPANCY	
						MAIN BUILDING CONSTRUCTION														

Rendering of building exterior



Site Plan

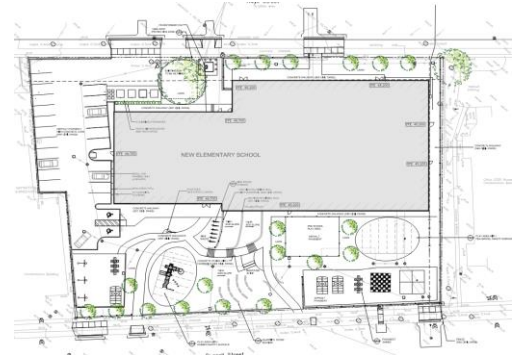

Aerial photo of site



Excavation & rock breaking for foundations



PROJECT STATUS

- Excavation of foundations ongoing
- Formwork for foundations to begin in early September
