



**EASTERN SHORE DISTRICT 7-12 SCHOOL
PROJECT STATUS REPORT
May 2023**

| |
|--|
| New grades 7-12 school project in East Chezzetcook to replace the existing Gaetz Brook JH & Eastern Shore District High Schools |
| Modern learning environment, accommodating 21st Century approaches to learning. |
| Public area with integrated hands-on, "maker", trades and technology spaces |
| 2 classroom wings w/ open, collaborative spaces |

| General Project Information | | Contacts re: concerns or questions | |
|-----------------------------|--|------------------------------------|---|
| Project Sponsor Group | NS Dept. of Public Works NS Dept. of Education and Early Childhood Development Halifax Regional Centre for Education | Construction related | Cameron Brow, Marco Site Superintendent, During regular business hours at 902-225-5503 or cbrow@marco.ca |
| Design Consulting | Harvey Architecture | General Project | David Webber, DPW Project Manager During regular business hours at 902-219-1521 or david.webber@novascotia.ca |
| General Contractor | Marco Construction | | |

| 2023 | | | | | | | | | | 2024 | | | | | | | | | |
|---------------------|----------------------------|-----|--------------|-----|--|---|-----|-----|-----------|--------------|-----|-----|-----|-----|-----|-----|------------------------------------|------------------|-----|
| 2022-23 SCHOOL YEAR | | | SUMMER BREAK | | 2023-24 SCHOOL YEAR | | | | | SUMMER BREAK | | | | | | | | | |
| Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | CHRISTMAS | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct |
| | | | | | ◆ Sports Field Construction Complete | | | | | | | | | | | | ◆ Sports Field Ready for Use | | |
| CURRENT MONTH | MAIN BUILDING CONSTRUCTION | | | | | | | | | | | | | | | | | TARGET OCCUPANCY | |
| | | | | | | ◆ Exterior building components complete | | | | | | | | | | | | | |


Rendering of approach to main entrance



Construction progress of interior walls



Aerial photo from the north, looking towards the main entrance (taken mid-May, 2023)

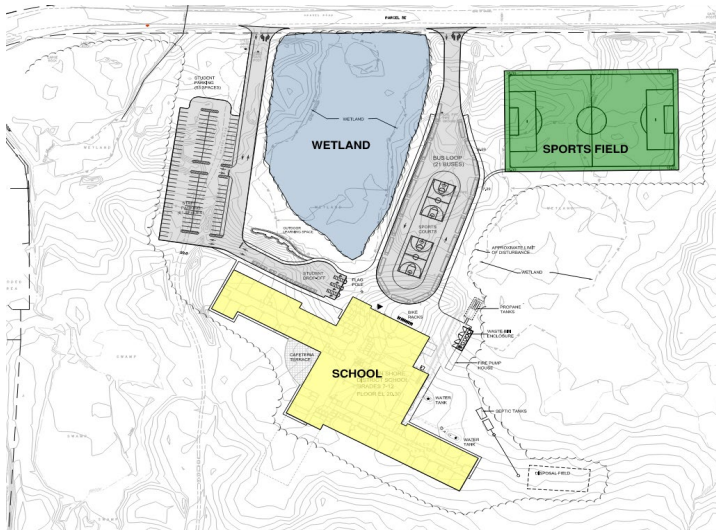

PROJECT STATUS

- Installation of foundations and load bearing masonry walls ongoing
- Remaining architectural trade packages to be awarded
