


**ST. JOSEPH'S A. MCKAY ELEMENTARY SCHOOL  
PROJECT STATUS REPORT  
April 2024**

<b>New grades PP-6 replacement school project in north end Halifax</b>			
Modern, daylight filled learning environment, maximizing use of existing site Main floor area, accessible for after hours public use Large, central atrium, connecting all floors Integrated childcare centre Classroom areas w/ open, collaborative spaces			
<b>General Project Information</b>		<b>Contacts re: concerns or questions</b>	
Project Sponsor Group	NS Dept. of Public Works NS Dept. of Education and Early Childhood Development Halifax Regional Centre for Education	Construction related	John Rhynold, Marco Site Superintendent, During regular business hours at 902-209-4399 or jrhynold@marcogroup.ca
Design Consultant	Stantec Architecture Ltd.	General Project	Ed Burley, DPW Project Manager During regular business hours at 902-483-6143 or ed.burley@novascotia.ca
General Contractor	Marco Group		

**Rendering of building exterior**



**Site Plan**

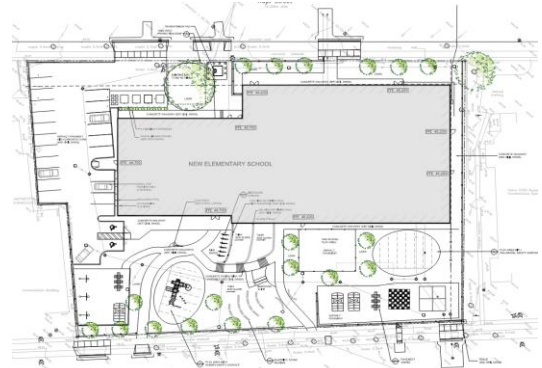

**Structural Steel & Foundations**



2024												2025											
2023-2024 SCHOOL YEAR					SUMMER		2024-25 SCHOOL YEAR					SUMMER		2025-26 SCHOOL YEAR									
J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
<b>CURRENT MONTH</b>					<b>MAIN BUILDING CONSTRUCTION</b>												<b>Substantial Completion</b>						

**PROJECT STATUS**

- Construction of foundations ongoing.
- Structural steel installation ongoing.

**SAFETY NOTICE**

This is an active construction site. No persons are allowed on site without appropriate protective equipment as directed by the Marco Group construction signage posted at site entrances. If you have an issue that you wish to discuss, please contact the appropriate person as listed above.

**Marco Group will make every effort to minimize impacts on neighbours and will follow municipal construction guidelines including traffic control, and noise restrictions.**
